


Lab 2: Agile Backlog Creation & Sprint Simulation in jira
Project: Remote Team Time Tracking & Project Approver
Jira Space: SELAB2

Name: Krish Yadav	SRN: PES1UG24CS234	Section : D
--------------------------	---------------------------	--------------------

1. Backlog - Epics and User Stories

The Jira backlog was organized into five major functional areas: Time Logging, Timesheet Submission, Timesheet Review, Timesheet Approval & Rejection, and Project Budget Usage. Each epic contains user stories representing the expected functionality of the system.

The backlog was used as the starting point for sprint planning. The stories were given priorities and later assigned story points according to their relative complexity.

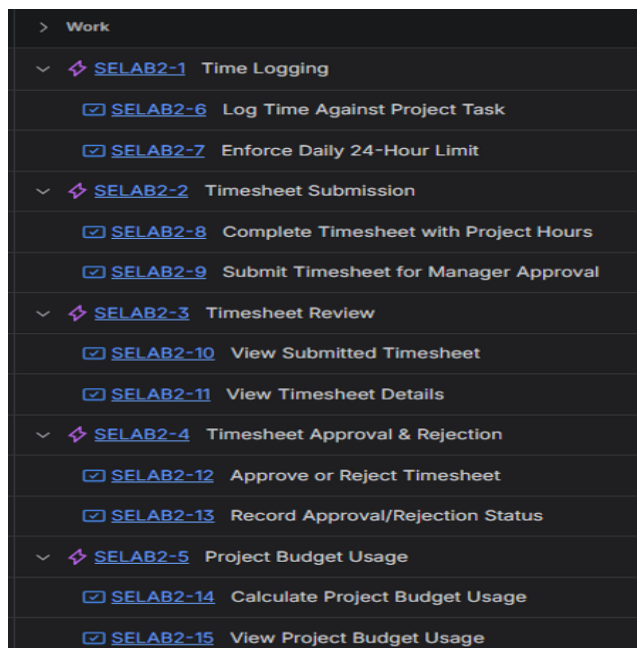

2. Story Point Assignments

Story points were assigned using a relative estimation approach based on the complexity and effort required to complete each user story. The estimates used in the Jira board include 3, 5 and 8 point stories.

For Sprint 1, the selected stories were SELAB2-6, SELAB2-7, SELAB2-8, SELAB2-9 and SELAB2-10, with story points of 3, 5, 3, 5 and 3 respectively, for a total of 19 story points.

For Sprint 2, the work focused on timesheet review, approval/rejection and project budget usage. The selected stories include SELAB2-11, SELAB2-12, SELAB2-13, SELAB2-14 and SELAB2-15, with estimates of 5, 5, 3, 8 and 3 story points respectively.

	Work	Assignee	Reporter	Priority	Status	Resolution	Created	Updated	Due date	Story Points	
☐	SELAB2-1 Time Logging	Unassigned	Krish Yadav	Medium	To Do	Unresolved	Aug 28, 2026, 3:10 PM	Aug 28, 2026, 3:10 PM	None	None	↔
☐	SELAB2-6 Log Time Against Project Task	Unassigned	Krish Yadav	High	Done	Unresolved	Sep 01, 2026, 10:44 PM	Sep 01, 2026, 11:11 PM	None	3	↔
☐	SELAB2-7 Enforce Daily 24-Hour Limit	Unassigned	Krish Yadav	High	Done	Unresolved	Sep 01, 2026, 10:46 PM	Sep 01, 2026, 11:12 PM	None	5	↔
☐	SELAB2-2 Timesheet Submission	Unassigned	Krish Yadav	Medium	To Do	Unresolved	Aug 28, 2026, 3:10 PM	Aug 28, 2026, 3:10 PM	None	None	↔
☐	SELAB2-8 Complete Timesheet with Project Hours	Unassigned	Krish Yadav	High	Done	Unresolved	Sep 01, 2026, 10:48 PM	Sep 01, 2026, 11:12 PM	None	3	↔
☐	SELAB2-9 Submit Timesheet for Manager Approval	Unassigned	Krish Yadav	High	Done	Unresolved	Sep 01, 2026, 10:48 PM	Sep 01, 2026, 11:13 PM	None	5	↔
☐	SELAB2-3 Timesheet Review	Unassigned	Krish Yadav	Medium	To Do	Unresolved	Aug 28, 2026, 3:11 PM	Sep 01, 2026, 10:36 PM	None	None	↔
☐	SELAB2-10 View Submitted Timesheet	Unassigned	Krish Yadav	Medium	Done	Unresolved	Sep 01, 2026, 10:49 PM	Sep 01, 2026, 11:13 PM	None	3	↔
☐	SELAB2-11 View Timesheet Details	Unassigned	Krish Yadav	High	Done	Unresolved	Sep 01, 2026, 10:50 PM	Sep 01, 2026, 11:58 PM	None	5	↔
☐	SELAB2-4 Timesheet Approval & Rejection	Unassigned	Krish Yadav	Medium	To Do	Unresolved	Aug 28, 2026, 3:11 PM	Sep 01, 2026, 10:36 PM	None	None	↔
☐	SELAB2-12 Approve or Reject Timesheet	Unassigned	Krish Yadav	High	Done	Unresolved	Sep 01, 2026, 10:52 PM	Sep 02, 2026, 12:04 AM	None	5	↔
☐	SELAB2-13 Record Approval/Rejection Status	Unassigned	Krish Yadav	Medium	Done	Unresolved	Sep 01, 2026, 10:52 PM	Sep 02, 2026, 1:15 AM	None	3	↔
☐	SELAB2-5 Project Budget Usage	Unassigned	Krish Yadav	Medium	To Do	Unresolved	Sep 01, 2026, 10:39 PM	Sep 01, 2026, 10:39 PM	None	None	↔
☐	SELAB2-14 Calculate Project Budget Usage	Unassigned	Krish Yadav	High	Done	Unresolved	Sep 01, 2026, 10:54 PM	Sep 03, 2026, 12:26 PM	None	8	↔
☐	SELAB2-15 View Project Budget Usage	Unassigned	Krish Yadav	Medium	Done	Unresolved	Sep 01, 2026, 10:54 PM	Sep 03, 2026, 12:26 PM	None	3	↔

3. Sprint Board (Active Sprint View)

The Active Sprint board was used to visualize work as it progressed through the workflow. The board is divided into To Do, In Progress and Done columns. Moving issues between these columns provides a visual representation of sprint progress.

The Jira evidence shows completed stories in the Done column and demonstrates how the board can be used to track the status of sprint work


The screenshot shows the Jira interface for the 'SELAB2 board'. The 'Active sprints' tab is selected, displaying a Kanban board with three columns: 'TO DO', 'IN PROGRESS', and 'DONE'. The 'TO DO' column is empty. The 'IN PROGRESS' column is empty. The 'DONE' column contains five completed stories, each with a title, a status bar, and a story key. The stories are: 'View Timesheet Details' (Timesheet Review, SELAB2-11), 'Approve or Reject Timesheet' (Timesheet Approval & Rejection, SELAB2-12), 'Record Approval/Rejection Status' (Timesheet Approval & Rejection, SELAB2-13), 'Calculate Project Budget Usage' (Project Budget Usage, SELAB2-14), and 'View Project Budget Usage' (Project Budget Usage, SELAB2-15). The board also includes a search bar, filters, and a 'Complete sprint' button.

4. Burndown Charts

The burndown chart compares remaining story points with the ideal guideline over the duration of a sprint. It provides a visual indication of how quickly the planned work is being completed.


Sprint 1

Sprint 1 began with 19 story points. The completed issues reduced the remaining work to zero. The Jira burndown therefore shows a rapid reduction in remaining work rather than a gradual decline across the full sprint duration.

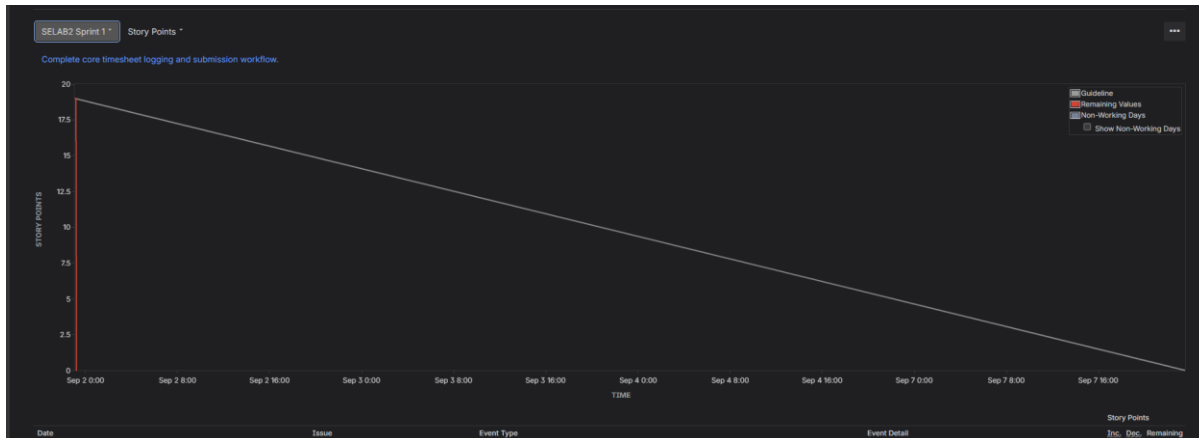

Sprint 2


Sprint 2 covered the timesheet review, approval/rejection and project budget workflow. The Jira burndown evidence shows the remaining-value line at the lower end of the chart rather than following the ideal guideline in a smooth progression.

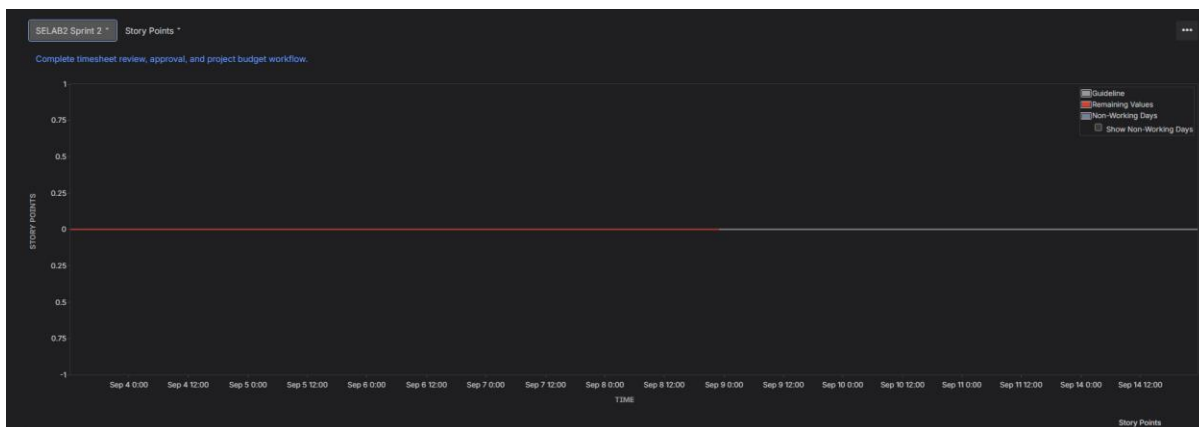

5. Sprint Reports


Sprint 1 Report

The Sprint 1 report records completion of the five selected stories: Log Time Against Project Task, Enforce Daily 24-Hour Limit, Complete Timesheet with Project Hours, Submit Timesheet for Manager Approval, and View Submitted Timesheet. Together, these stories represent 19 story points.

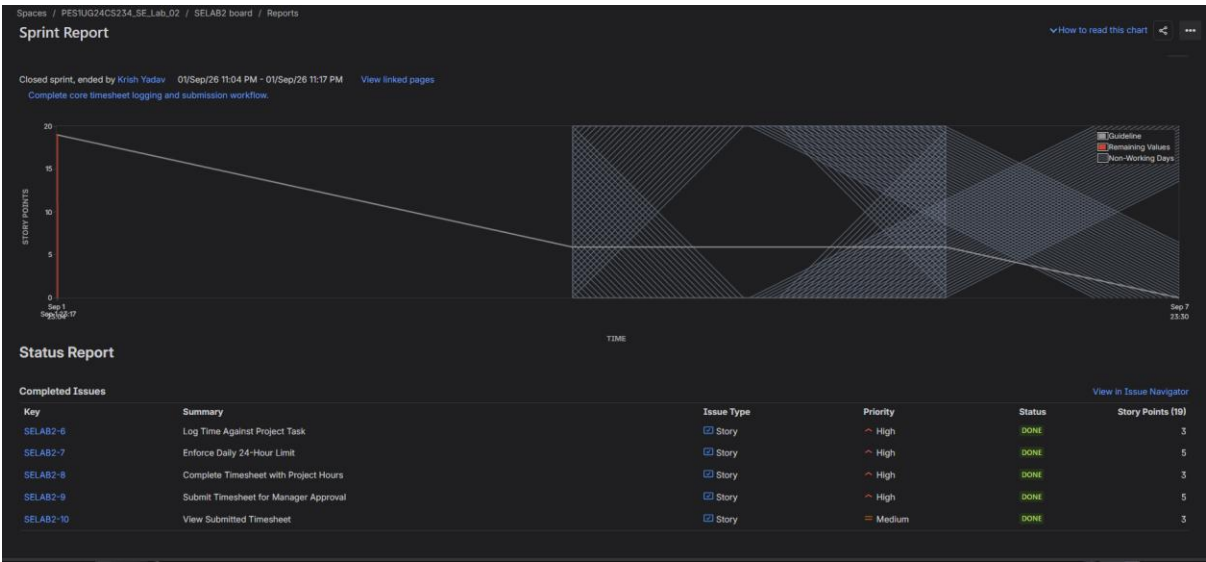

Sprint 2 Report

The Sprint 2 report covers the next stage of the workflow: reviewing submitted timesheets, approving or rejecting them, recording the approval/rejection status, and calculating and viewing project budget usage. The report also records issues that were not completed within the sprint and issues completed outside the sprint.

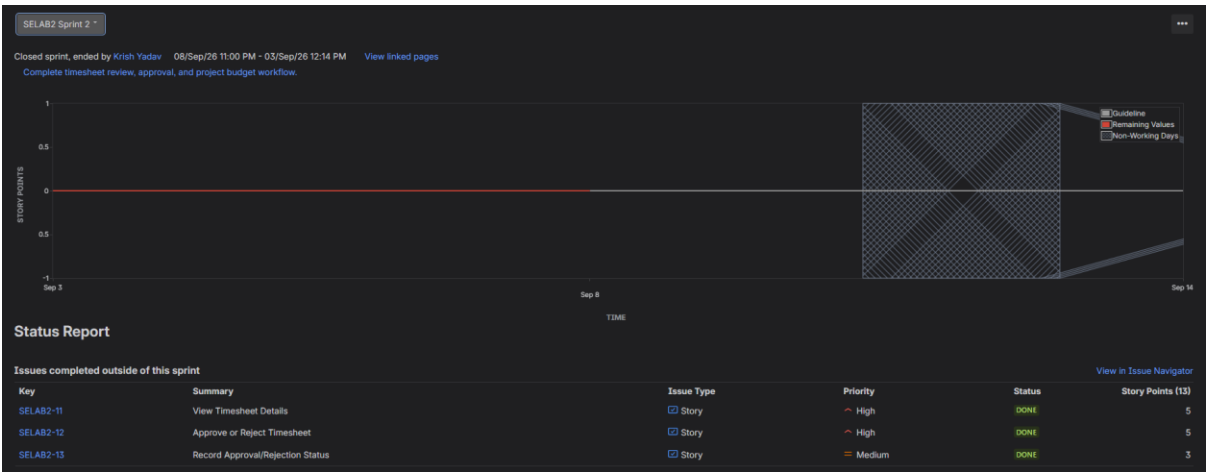

6. Reflection

1. Did your estimations reflect the actual effort?

The story-point estimates provided a reasonable indication of relative complexity. Smaller stories such as viewing submitted information were estimated at 3 points, while more involved functionality such as enforcing the daily time limit, submitting a timesheet for approval, and calculating project budget usage received higher estimates. Since this was a simulated Agile exercise, the points primarily represented expected relative effort rather than measured development time.

2. Was your backlog well-prioritized?

The backlog was organized around the main workflow of the system. Time logging and timesheet submission form the foundation, followed by review and approval/rejection, and finally project budget usage. High-priority stories were used for important workflow operations, while medium-priority stories supported viewing and status-related functionality. This ordering provides a logical progression from entering work to reviewing and managing its financial impact.

3. How did your simulated sprint align with your plan?

Sprint 1 successfully completed the five planned stories and reduced the remaining story points to zero in the Jira burndown evidence. Sprint 2 was used for the next group of workflow features. The Sprint 2 report shows that some items were completed outside the sprint while other items remained incomplete at the time the sprint was closed. This demonstrates the importance of tracking work continuously rather than relying only on the final sprint state.

4. What insights did the burndown chart give about your team's capacity?

The burndown charts show that the timing of status updates has a strong effect on how the team's progress appears. When several stories are moved to Done within a short period, the remaining-work line drops sharply instead of following the ideal guideline gradually. Therefore, the chart is most useful when the board is updated continuously throughout the sprint. The exercise also helped illustrate how story points can be used to compare planned workload with the amount of work remaining.

7. Conclusion

The Jira exercise demonstrated the complete basic Agile workflow: creating and organizing a backlog, assigning story points, planning and executing sprints, tracking issues on an Active Sprint board, and interpreting burndown and sprint reports. The project backlog was divided into functional epics and the work was distributed across Sprint 1 and Sprint 2. The resulting Jira reports provide evidence of completed work and unfinished or outside-sprint work.
